

# BRIDGE STREET FRONT PORCH

WACO CITY COUNCIL WORK SESSION, SEPTEMBER 1, 2020







## CONCEPT WORKSHOPPED WITH FOCUS GROUPS




## PROPOSED PROJECT TODAY




## **100 Block**

- Proposed crosswalk\*
- IOI Elm Apartments
- First seating area
- Cambria Hotel main entrance



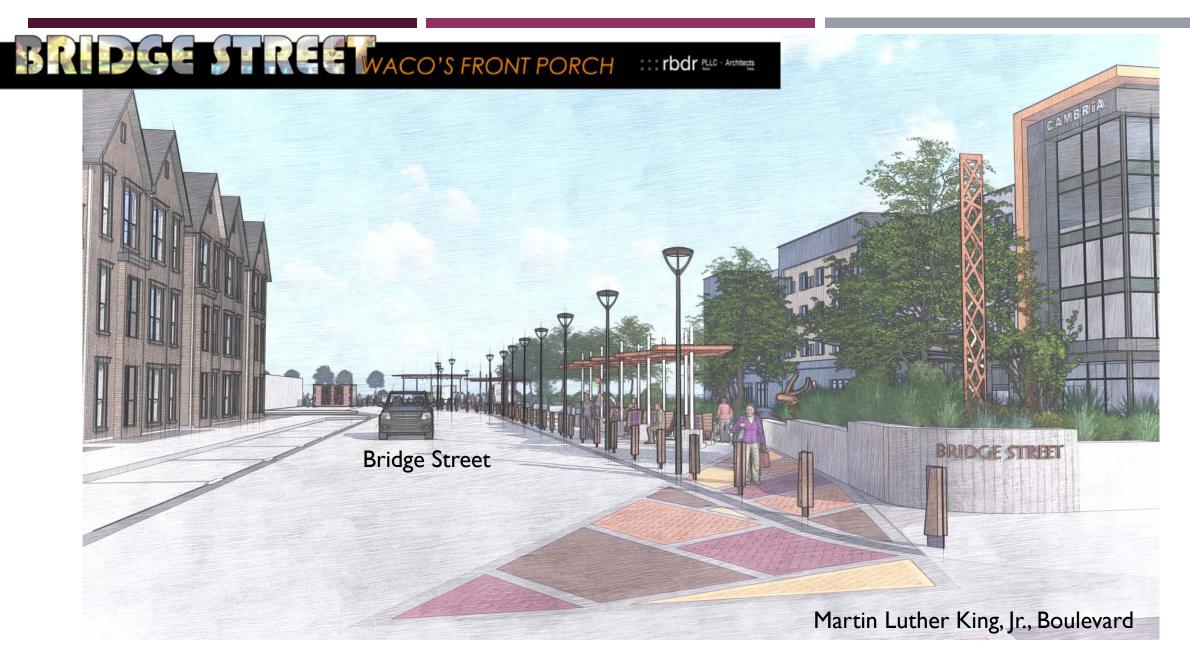



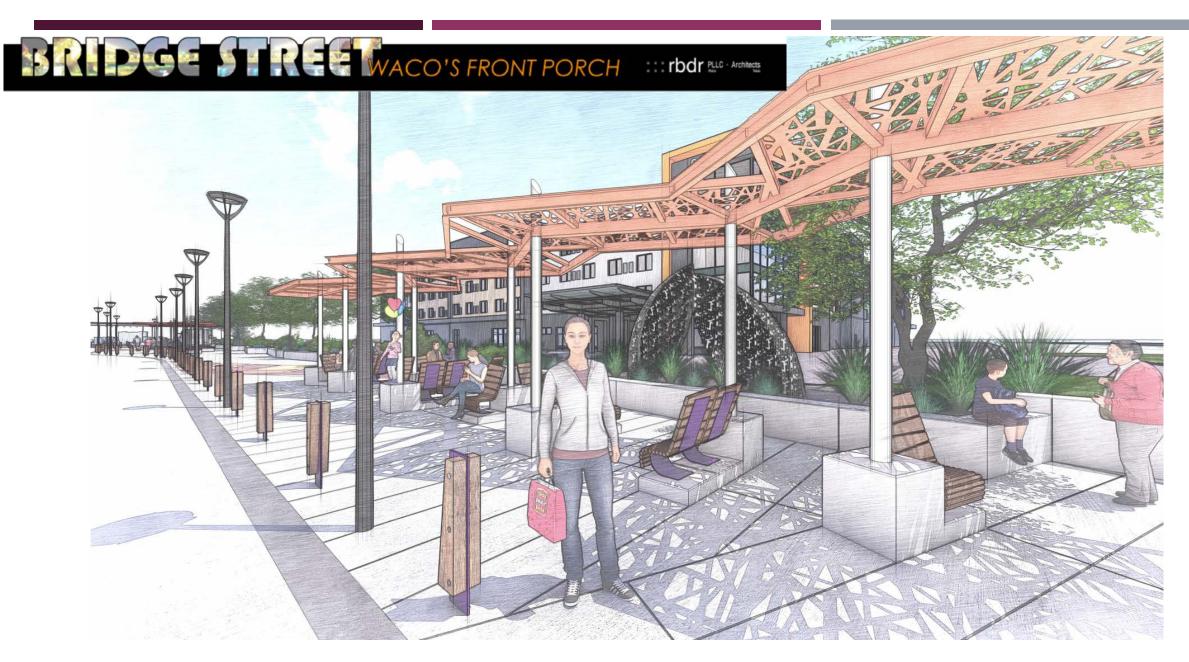




# 


## 200 Block

- Food truck and second seating area
- Empire Seed
- 209/211 Elm (City Center Waco owns)






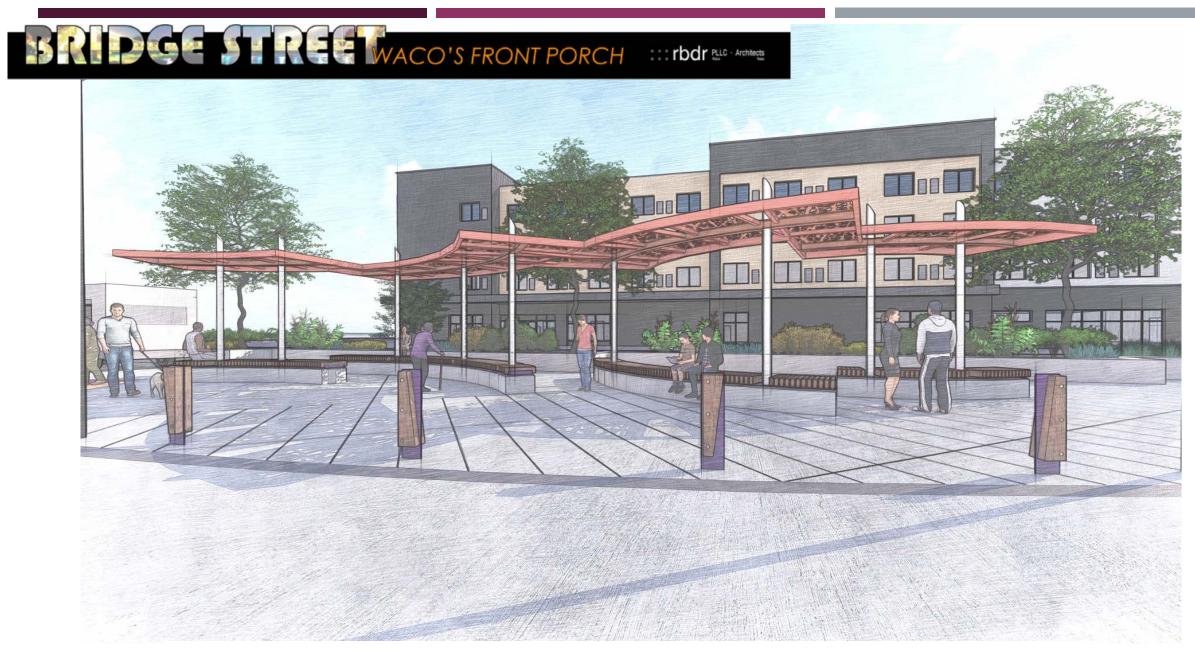

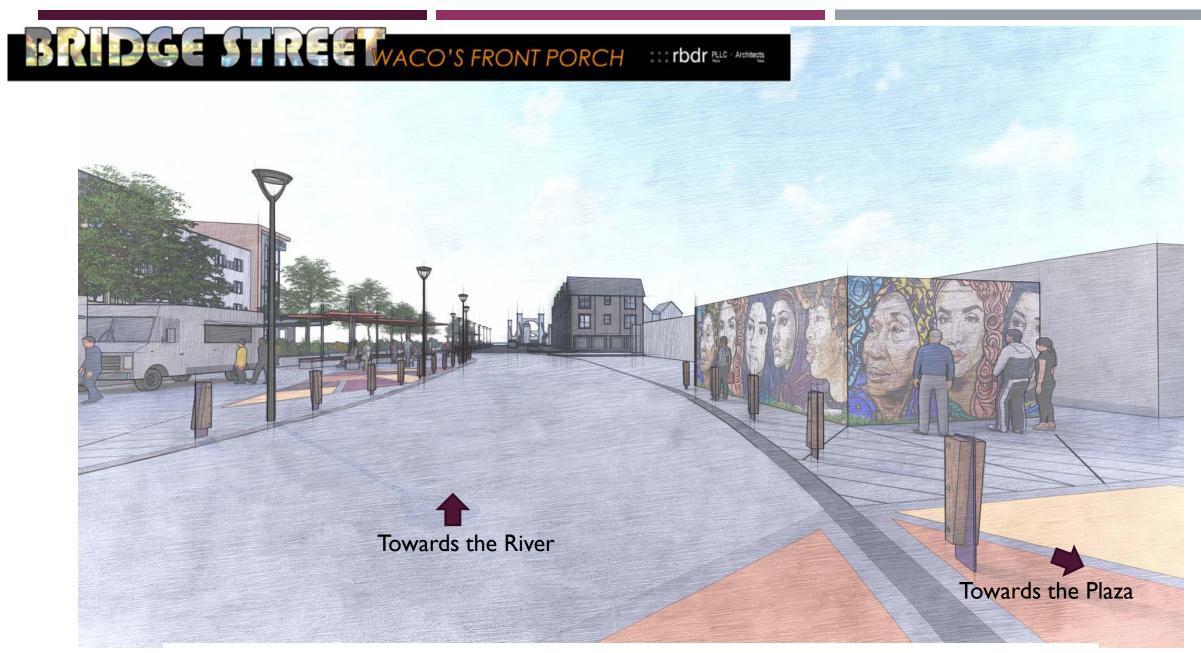



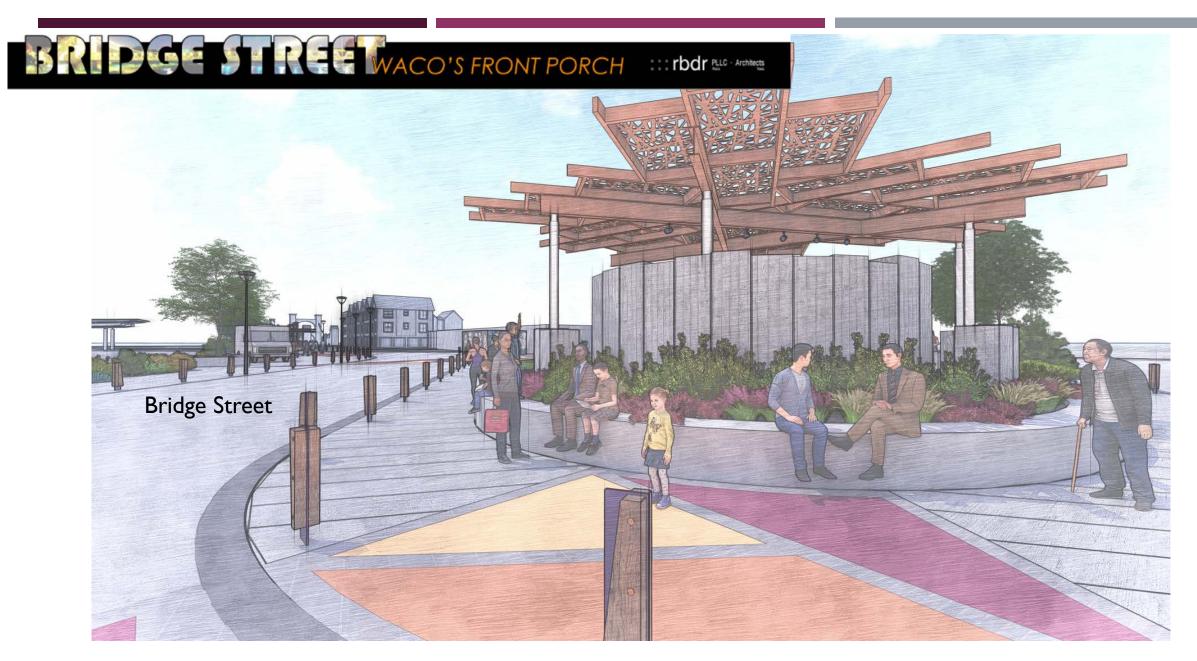

### TIMELINE

Phase	Main Elements	Design Complete	<b>Construction Complete</b>
Phase I	Wastewater Line	1/20/20	7/16/2020
Phase 2	Vehicular Pavement (completed, not fully open)	3/10/20	Current estimate: September 2020
Phase 3	Sidewalks/ Pedestrian Pavement	5/21/20	Current estimate: January 2021
Phase 4	Structures, Landscaping and Crosswalk	8/19/20	Under review


### BUDGET

Funding Source	Amount	Main Components	Status
TIF Award/ Design	\$ 350,000	Professional Services	Anticipated completion October with contingency through November 23
TIF Award/ Construction	\$5,548,000	<ul> <li>Festival Street</li> <li>Concrete Paving</li> <li>Reinforced sidewalk</li> <li>Storm drain</li> <li>New parking areas</li> <li>Replacing curb &amp; gutter</li> <li>New lighting</li> <li>ADA improvements</li> </ul>	<ul> <li>Crosswalk is an alternate bid and under review</li> <li>Public art is not included but surfaces and bases for future installation are included</li> </ul>
380 Agreement/ Sewer Line	\$ 571,553	Wastewater Line	Complete; funded construction only








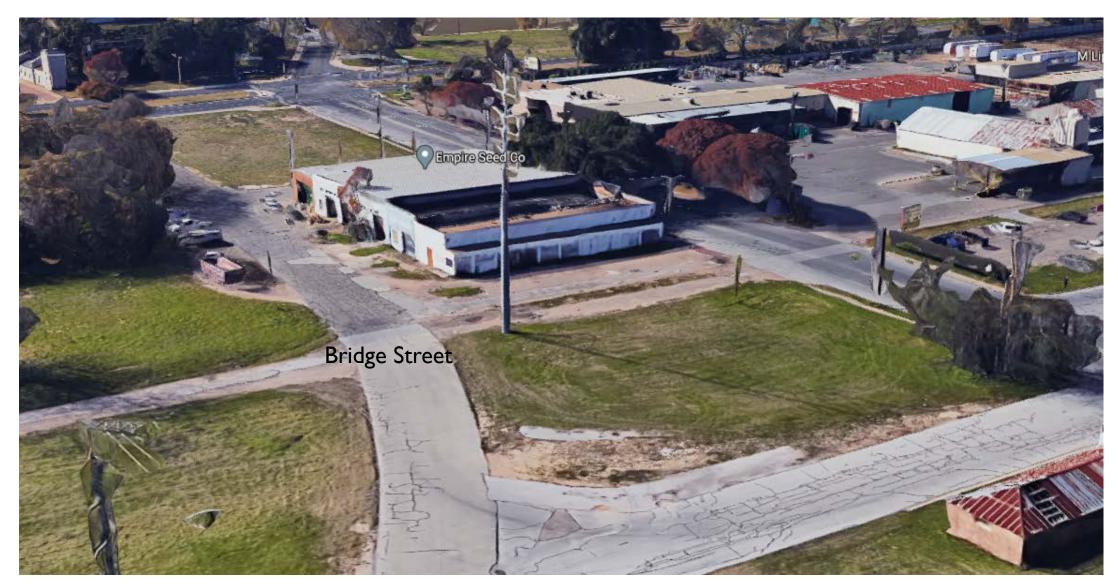

City Center Waco: a bridge between development and the community



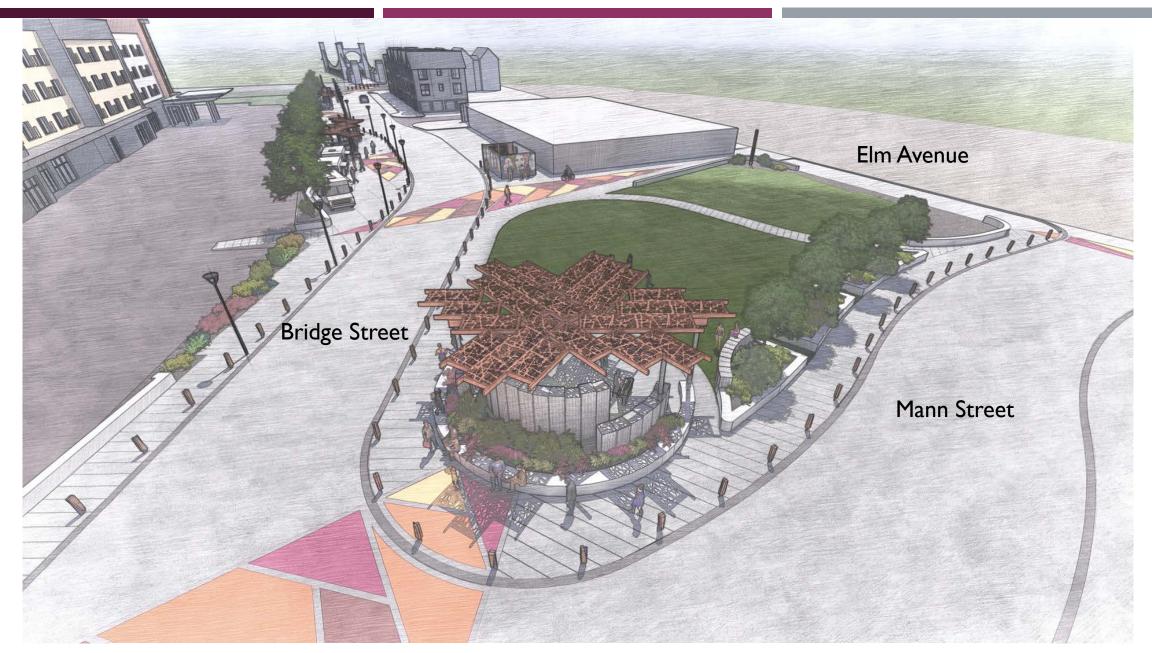

City Center Waco: a bridge between development and the community

## Questions?

# Thank you!
